



DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	19-Apr-09	280

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranjit Sahu	sahur@earthlink.net	702-567-0400
CLIENT, PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.com	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolutions.com	720-641-8660

WEATHER CONDITIONS

Conditions	Temp (°F)	Wind	Adt'l Readings
Alt: Sunny/Clear	60	7 mph	Humidity: 45%
High: 65	65	7 mph	Humidity: 45%
Additional Weather Comments: Calm - 7 mph. Night Shift.			

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Dick Laubinger	Construction Manager	Construction Management Services	N
Dan Brennecke	Project Manager, CM	Construction Management Services	N
Richard Davis	Project Engineer	Construction Management Services	N
Chris White	Assist. Const. Mgr	Construction Management Services	N
Wayne Hodgson	Assist. Const. Mgr	Construction Management Services	Y
Kevin Cooke	Assist. Const. Mgr	Construction Management Services	Y
Jane Laubinger	Admin Assistant	Construction Management Services	N

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Greg Corcoran	Design Engineer	Oversight	N
Dan Street	QA Manager	Oversight	N
Jim Cox	QA/QC Supervisor	Oversight	N
Rebecca Flynn	Engineer	Oversight	N
Sam Campbell-Nelson	QA/QC Tech	Oversight	N
Roland Derosier	QA/QC Tech	Oversight	Y
Camron Liddell	QA/QC Tech	Oversight	N
Victor Heredia	QA/QC Tech	Oversight	N

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N
Jerry Faucheur, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Mark Eisman, ASW	Inspector	Linear Inspector	N
Darin Gordon, McKinley	Oversight	For NDEP	Y
Dock Kim, ATC	Field Observation	For AIG	N
Joe Ludlow, ASW	Inspector	Linear Inspector	N
Steve Morrow, ASW	Inspector	Linear Inspector	N
Brian Rakvica	Inspector	NDEP	N
PBS&J, Survey	Surveyors	Survey	N

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N
Erik Geringer	Entact	Project Manager	N
Jeremy Schissler	Entact	Acting Project Manager	N
Josh Carrol	Entact	Asst Project Manager	Y
Michael Carlson	Entact	Engineer	N
Joe Cullis	Entact	Health & Safety Officer	Y
Timothy Stahl	Entact	Health and Safety Technician	N
Ed Long	Entact	48 Equipment Operators & Truck Drivers	Y
Lance Bruce	Entact	CAMU, Superintendent	N
Terry Harper	Entact	Health & Safety Officer	Y
Rick McIntire	Entact	CAMU, Superintendent	Y
Dale Walsh	Converse	CSP, Safety	N
Ell Blackburn	Entact	Asst Project Manager	N
	Environmental Specialties, Inc.	1 Liner Superintendent	N
	Environmental Specialties, Inc.	12 Laborer/Scammers	N
Carol McIntire	Entact	Health & Safety Officer	Y
Roger Wagner	Entact	Eastside, Superintendent, Night Shift.	Y
	ABC Survey	Eastside/CAMU	Y
	Foundation Pile, Inc. (6)	Mobilized on site, removing sheets at SW-2.	N
Russell Karnes	Entact	Superintendent	N

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed	Y/N
CAT D400E Dump Truck (10)		CAMU	-
JD D400 Dump Trucks (10)		Eastside	-
CAT 324D long stick excavator		Eastside	-
CAT D6R Dozer with disc, (1)		Eastside	-
CAT 345 excavators, (8)		Eastside and CAMU, Southern rib	-
CAT 330 Excavator (1)		CAMU	-
Kobelco Excavator, (1)		CAMU	-
CAT D8 LGP Dozer (1)		Eastside	-
Water Trucks (3)		Eastside	-
Case backhoe		CAMU	-
CAT 16H Grader		CAMU	-
CAT D-10 Dozer		CAMU	-
Water Trucks (4)		CAMU	-
CAT D-8 Dozer, (3)		CAMU	-
CAT 14H Grader		CAMU	-
Grass		CAMU	-
JLG		CAMU	-
Smooth drum Rollers, (3)		CAMU	-
Tenard Street Sweeper		Eastside and CAMU	-
Komatsu Loader		CAMU, Phase 1	-
Chieftain 1400 Powerscreener		CAMU	-
(1) Crane		Removing sheetpiles (1) Crane.	-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOI's	Purpose	Delivery Restrictions
GCL	CETCO	0	rolls	For CAMU, On site	1612

DAILY PRODUCTION & QUALITY CONTROL REPORT					
Project No./Contract No.	Project Title / Location			Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation			19-Apr-09	280
Geocomposite	Agri	0	rolls	For CAMU, On site	2373
Geomembrane	Agri	0	rolls	For CAMU, On site	514

WORK COMPLETED
Description of Work Executed Today:
Eastside Mixing and Drying Activity:
Day Shift:
- No Activity.
Night Shift:
- Hauled material from HP-2 and Beta ditch.
CAMU Activity:
Day Shift:
- No Activity.
Night Shift:
- Continued placing material in Phase II and IIA.
Embankment
- Phase I embankment, complete.
- Phase I estimated cumulative embankment placed:
- Phase II embankment, complete.
Sump/Vadose Monitoring: Phase I: LCRS Sump: Measurement taken: (N/A). Water Pumped: N/A.
Vadose: Measurement taken: (N/A). Water Pumped: N/A.
Phase II: LCRS Sump: Measurement taken: (N/A). Water Pumped: N/A.
Vadose: N/A.
Inspections: CAMU: Weston monitored sump access: N/A.
Eastside: Perimeter fence, N/A.

Estimated Waste Placement (Estimated volumes do not account for shrinkage due to loss of moisture on wet ponds)

Phase I		
Previous Daily Cumulative =		291,200 cy
Operations layer placed (completed) for liner certification = 21,662		0 cy
Daily Day shift waste placed today: Phase IV,V scape & Phase IIIB trench excavation. 0 loads @ 20 cy/load (0 trucks) =		0 cy
Daily Night shift placed today: 0 loads @ 18cy/load (0 trucks) =		0 cy
To Date Phase I estimated cumulative waste placed =		291,200 cy
Phase II		
Previous Daily Cumulative =		524,100 cy
Operations layer placed (completed) for liner certification = 37,188		0 cy
Daily Day shift waste placed today: Parcel 4B/Mohawk Drive. (0) loads @ 18 cy/load (0) trucks =		0 cy
Daily Day shift waste placed today: Silt Trenches, (0) loads @ 18cy/load (0) trucks =		0 cy
Daily Night shift placed today: (60) loads @ 18cy/load (10) trucks =		1,080 cy
To Date Phase II estimated cumulative waste placed =		525,180 cy
Phase IIIA		
Previous Daily Cumulative =		78,390 cy
Operations layer placed directly in Phase IIIA today: (0) loads @ 18 cy/load (0) trucks =		0 cy
Operations layer placed (completed for liner certification = 21,276		0 cy
Daily Day shift waste placed today: From Phase IIIB. (0) loads @ 18 cy/load (0) trucks =		0 cy
Daily Night shift waste placed today: (222) loads @ 18cy/load (18) trucks =		3,996 cy
To Date Phase IIIA estimated cumulative waste placed =		82,386 cy

Cummulative Total To Date All Phases =	898,766 cy	Estimated Waste at Completion (cy)	2,050,000	% Complete	43.8%
---	-------------------	---	------------------	-------------------	--------------

Geosynthetics Placed

	Previous	Placed	Cummulative
Phase I (complete)			
GCL	307,372	0	307,372
Geomembrane	307,372	0	307,372
Geocomposite	307,372	0	307,372
Geotextile	68,340	0	68,340
Phase II (complete)			
GCL	498,468	0	498,468
Geomembrane	498,468	0	498,468
Geocomposite	520,592	0	520,592
Geotextile	0	0	0
Phase IIIA			
GCL	221,000	0	221,000
Geomembrane	221,000	0	221,000
Geocomposite	221,000	0	221,000
Geotextile	20,000	0	20,000
Phase IIIB			
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase IV			
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase V			
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	19-Apr-09	280

DAILY PHOTO LOG

Photo 1




CAMU: Phase IIIA in front. Erecting crane in background.

Photo 2



Eastside: Southern Rib.

Photo 3

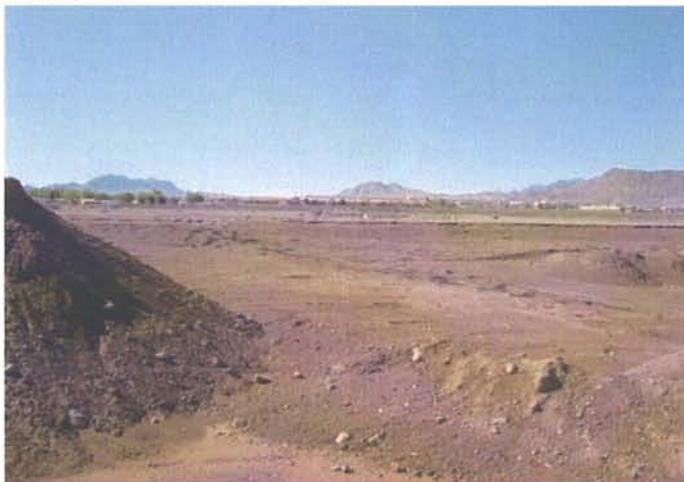

Eastside: Southern Rib.

Photo 4



Eastside: Southern Rib, presoaking.
