

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	16-Oct-08	103

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris,	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranajit Sahu	sahuron@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.c	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolution	720-641-8660

WEATHER CONDITIONS

Conditions				Temp (°F)	Wind	Add'l Readings	
AM	Sunny/Clear	PM	Sunny/Clear	Low 54 High 84	S 3mph	Precip. (inches)	Humidity (%)

Additional Weather Comments

Calm in AM, 3 mph from the South in PM.

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Dick Laubinger	Construction Manager	Construction Management Services.	Y
Dan Brennecke	Project Manager, CM	Construction Management Services.	Y
Dave Goertz	Project Engineer	Construction Management Services.	N
Richard Davis	Project Engineer	Construction Management Services.	Y
Chris White	Assist. Const. Mgr	Construction Management Services.	Y
	Assist. Const. Mgr	Construction Management Services.	
June Laubinger	Admin Assistant	Construction Management Services.	Y

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Greg Corcoran	Design Engineer	Oversight	N
Dan Street	QA Manager	Oversight	Y
Jim Cox	QA/QC Supervisor	Oversight	N
Robecca Flynn	Engineer	Oversight	N
Wayne Wofford	QA/QC Tech	Oversight	Y
Brent Barbacane	QA/QC Tech	Oversight	Y
Camron Liddell	QA/QC Tech	Oversight	Y

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring.	N
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring.	Y
Jerry Fauchaux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Scott McKeag, McGinley	Oversight	For NDEP	N
Devin Gordon, McGinley	Oversight	For NDEP	Y
Jennifer Coe, ATC	Field Observation	For AIG	Y
Ron Perry, ASW	Inspector	Liner Inspector	N
PBS&J, Survey	Surveyors	Surveying, Set points at North BMI landfill Northwest corner.	Y
Brian Rakvica	Inspector	NDEP	N

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N
Erik Geringer	Entact	Project Manager	Y
Josh Carrol	Entact	Asst Project Manager	Y
Russ Karnes	Entact	Eastside, Superintendent	Y
Michael Carlson	Entact	Engineer	Y
Joe Curilla	Entact	Health & Safety Officer	N
Timothy Stadt	Entact	Health and Safety Technician	Y
	Entact	26 Equipment Operators & Truck Drivers	Y
Ed Long	Entact	CAMU, Superintendent	Y
Adam Calveledge	Entact	Health & Safety Officer	Y
Rick McIntire	Entact	CSP, Safety	Y
	American Asphalt	1 Equipment operators	Y
	American Asphalt	1 Superintendent	Y
	Environmental Specialties, Inc	Liner Superintendent	N

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	16-Oct-08	103

Environmental Specialties, Inc.	Laborers/ Seammers	N	
Kenney Survey	CAMU	N	
ABC Survey	Eastside/CAMU	N	

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (2)		CAMU	-	-	-	-
JD D400 Dump Trucks (8)		Eastside		-	-	-
CAT 324D long stick excavator		CAMU	-	-	-	-
CAT D8R Dozer with disc		Eastside		-	-	-
CAT 345 excavator		Eastside		-	-	-
CAT 330 Excavator		Eastside		-	-	-
Case double pan scrapers.		Eastside		-	-	-
CAT D6 LGP Dozer (2)		Eastside				-
Water Trucks (2)		Eastside				-
637/631 Cat Scrapers (6)		CAMU				-
CAT 16H Grader		CAMU				-
CAT D-10 Dozer		CAMU				-
CAT Water Wagon		CAMU				-
CAT D-6 Dozer		CAMU				-
CAT 14H Grader		CAMU				-
Gradall		CAMU				-
JLG		CAMU				-
IR Smooth drum Roller		CAMU, Phase 1				-
Tenent Street Sweeper		Eastside and CAMU				-
Bomag Smooth drum Roller		CAMU, Phase 1				-
						-
						-
						-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOM	Purpose	Delivery Verification			
					to date	Qty	Spec	Tags
GCL	CETCO	0	rolls	For CAMU, On site		207		
Geocomposite	Agru	0	rolls	For CAMU, On site		194		
Geomembrane	Agru	0	rolls	For CAMU, On site		37		

WORK COMPLETED

Description of Work Executed Today

Eastside Mixing and Drying Activity:

- D6 dozer spread wet material over dry ponds.
- Continued pumping water from SC-1 to SW-12.
- 324 CAT excavator mixing dry soils with wet soils in dry ponds.
- Conducted dust monitoring.
- Performed decontamination of equipment.
- Spread rock at trailers.

CAMU Activity:

Excavation .

- Phase II continued screening soils and placing lifts on floor. Continued working on east and south slopes.
- Continue construction of ramp in Phase 1. Hauled prepared 1" minus screened soils, placed as operations layer on slopes.
- Western ditch soils hauled into Phase 1. Day Shift: 220 loads @ 22 cy/loads = 4,840 cy (5) trucks.
- Western ditch soils hauled into Phase 1. Night Shift: 126 loads @ 22 cy/loads = 2,872 cy (4) trucks.
- Western ditch soils stockpile of 1" minus material loaded and placed in Phase 1. 82 loads @ 22cy/loads = 1,804 cy, (2) trucks.
- (2) D6 dozers placed western ditch soils in 12" lift. Followed by (2) vibratory rollers compacting (3) complete passes in Phase 1.
- Continued placing operations layer on West slope of Phase 1 (1" minus soils). CAT 330 excavator used to remove Woven Geotextile.
- Conducted dust monitoring.

Embankment

- Phase 1 embankment, complete.
- Phase 1 estimated cumulative embankment placed: 0 cy

Waste Placement

- Phase 1 estimated daily waste placed: 220 loads @ 22cy/load = 4,840 cy
- night shift placed: 126 loads @ 22cy/load = 2,872 cy
- Phase 1 estimated cumulative waste placed: 94,614 cy. Western Ditch Soils
- Phase 1 Operations Layer placed, completed. Cumulative total: 21,662

Geosynthetics. Estimated cumulative installed quantity by Phase.

- Phase 1 GCL placed: 0 sf daily, 307,372 sf cumulative.
- Phase 1 Geomembrane: 0 sf daily, 307,372 sf cumulative
- Phase 1 Geocomposite: 0 sf daily, 307,372 sf cumulative.
- Phase 1 Geotextile: (0) sf daily, 69,340 sf cumulative.

Basic Remediation Company

875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	16-Oct-08	103

DAILY PHOTO LOG

Photo 1



CAMU: Phase 1 West slope operations layer placed.

Photo 2




CAMU: Phase 1 Ramp in production.

Photo 3



CAMU: Phase 1, West floor, looking down ramp.

Photo 4

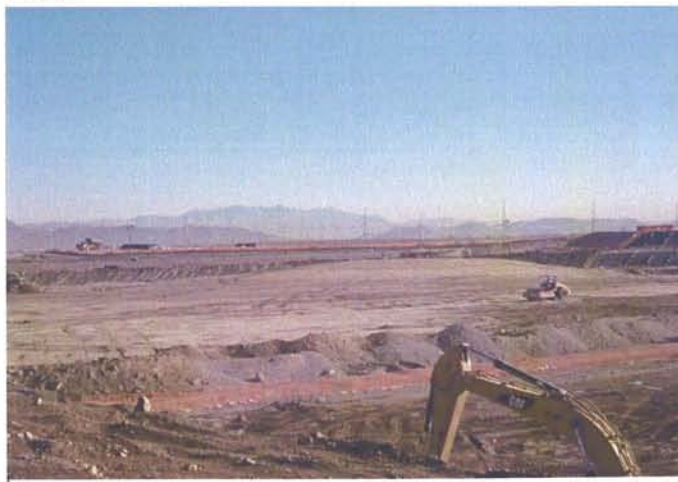

CAMU: Phase 1. looking east at Ramp.
