# Basic Remediation Company 875 West Warm Springs Road Henderson, Nevada 89011

Jerry Faucheux, Tetra Tech



Ν

N

## **DAILY PRODUCTION & QUALITY CONTROL REPORT**

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	22-Dec-08	165
		22-Dec-08	103

PROJECT POINTS OF CONTACT						
Position	Name	E-Mail Address	Phone No.			
BRC PROJECT MANAGER	Lee Farris	lfarris@landwellco.com	702-567-0400			
BRC PROJECT MANAGER	Ranajit Sahu	sahuron@earthlink.net	702-567-0400			
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.c	970-260-5886			
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolution	720-641-8660			

	Cond	itions		Tem	p (F)	W	ind	Add'l Readings
AM	Our / Darty Olaydly	PM	Curry / Dorty Claudly	Low	39			Precip. (In.Dy.)
AW	Sunny / Party Cloudly	1,111	Sunny / Party Cloudly	High	58	W	12mph	Humidity (%)

	Trade / Work Performed	Y/N
Construction Manager	Construction Management Services.	N
Project Manager. CM	Construction Management Services.	Y
Project Engineer	Construction Management Services.	Y
Assist. Const. Mgr	Construction Management Services.	Y
Assist. Const. Mgr	Construction Management Services.	Y
Assist. Const. Mgr	Construction Management Services.	Y
Admin Assistant	Construction Management Services.	N
	Project Manager. CM Project Engineer Assist. Const. Mgr Assist. Const. Mgr Assist. Const. Mgr	Project Manager. CM Construction Management Services. Project Engineer Construction Management Services. Assist. Const. Mgr Construction Management Services. Assist. Const. Mgr Construction Management Services. Assist. Const. Mgr Construction Management Services.

Name	Position	Trade / Work Performed	Y/N
Greg Corcoran	Design Engineer	Oversight	N
Dan Street	QA Manager	Oversight	Y
Jim Cox	QA/QC Supervisor	Oversight	N
Robecca Flynn	Engineer	Oversight	N
Wayne Wofford	QA/QC Tech	Oversight	Y
Roland Derosier	QA/QC Tech	Oversight	Y
Camon Liddell	QA/QC Tech	Oversight	Y
Jeremy Osborn	QA/QC Tech	Oversight	Y

#### ON-SITE SUPPORT PERSONNEL Name Position Trade / Work Performed Y/N Doug Herlocker, Tetra Tech Air Monitoring Specialist Air Monitoring, Set up new areas at CAMU Becky Dano, Tetra Tech Air Monitoring Specialist Air Monitoring, Air Monitoring

Air Monitoring Specialist

OVERSITE PERSONNE			
Name	Position	Trade / Work Performed	Y/N
Mark Eizman, ASW	Inspector	Liner Inspector	Y
Devin Gordon, McGinley	Oversight	For NDEP	Y
Dock Kim, ATC	Field Observation	For AIG	Y
Joe Ludlow, ASW	Inspector	Liner Inspector	N
Steve Morrow, ASW	Inspector	Liner Inspector	N
Brian Rakvica	Inspector	NDEP	N
PBS&J, Survey	Surveyors	Surveying, QA	N
ON OUTE CONTRACTOR	DEDCONNEL		SELECTION OF THE PARTY.

PBS&J, Survey	Surveyors	Surveying, QA	N
ON-SITE CONTRACT	OR PERSONNEL		
Name	Company	Trade / Work Performed	Y/N
Erik Geringer	Entact	Project Manager	N
Josh Carrol	Entact	Asst Project Manager	Y
Russ Karnes	Entact	Eastside, Superintendent	Y
Michael Carlson	Entact	Engineer	Y
Joe Curilla	Entact	Health & Safety Officer	Y
Timothy Stadt	Entact	Health and Safety Technician	Y
	Entact	26 Equipment Operators & Truck Drivers	Y
Ed Long	Entact	CAMU, Superintendent	Y
Lance Bruce	Entact	Health & Safety Officer	Y
Terry Harper	Entact	CAMU, Superintendent	Y
Rick McIntire	Entact	CSP, Safety	N
Dale Walsh	Converse	CSP, Safety	N

1 of 4 Ver 1.1 11/07

## **DAILY PRODUCTION & QUALITY CONTROL REPORT**

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	22-Dec-08	165
		22-Dec-08	105

Eli Blackburn	Entact	Asst Project Manager	Y
	Environmental Specialties,Inc	1 Liner Superintendent	Y
	Environmental Specialties,Inc	12 Laborers/ Seamers	Y
	Kenney Survey	CAMU	N
		Eastside/CAMU	N

ON-SITE EQUIPMENT		经营产品的特殊的				
Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (10)		CAMU	-	-	-	-
JD D400 Dump Trucks (9)		Eastside		-	-	-
CAT 324D long stick excavator		CAMU	- 1	-	-	-
CAT D8R Dozer with disc		Eastside		-	-	-
CAT 345 excavator, (3)		Eastside		-	-	-
CAT 330 Excavator		Eastside		-	-	-
Case double pan scrapers.		Eastside		-	-	-
CAT D6 LGP Dozer (1)		Eastside				-
Water Trucks (2)		Eastside				-
637/631 Cat Scrapers (2)		CAMU				-
CAT 16H Grader		CAMU				-
CAT D-10 Dozer		CAMU				-
CAT Water Trucks (2)		CAMU			-	
CAT D-6 Dozer, (2)		CAMU				-
CAT 14H Grader		CAMU				-
Gradall		CAMU				-
JLG		CAMU				-
IR Smooth drum Roller		CAMU, Phase 1				-
Tenent Street Sweeper		Eastside and CAMU				-
Bomag Smooth drum Roller		CAMU, Phase 1				-
Chieftain 1400 Powerscreener		Eastside, screening 1" minus				-

MATERIAL HANDLING	MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)							
Material	Vendor	Today	UOM	Purpose	Delivery Verification			
Waterial	Vendor	Today	OOW	Furpose	to date   Qty	Spec Tags		
GCL	CETCO	0	rolls	For CAMU, On site	506			
Geocomposite	Agru	0	rolls	For CAMU, On site	599			
Geomembrane	Agru	0	rolls	For CAMU, On site	192			

#### WORK COMPLETED

#### Eastside Mixing and Drying Activity:

- Day Shift:
- Mixing wet material into dry ponds
- Prepared for night haul operations
- Night Shift:
- Continued hauling material from HP-3 stockpile and PUB-4

#### CAMU Activity:

- Day Shift:
- ESI placed GCL and geomembrane on the North BMI Landfill
- Continued first lift push-out of 1-inch minus on the BMI North Landfill
  Continued screening at the 200,000cy stockpile and hauling to North BMI Landfill
  Continued 6\* scrape on Phase IIIB
- Prepared for night haul operations.
- Night Shift:
- Continued placing material in Phase 1.

- Phase 1 embankment, complete.
- Phase 1 estimated cummulative embankment placed: 0 cy
- Phase II embankment , complete.

#### Waste Placement

- Phase 1 estimated daily waste placed: 29 loads @ 20cy/load = 580cy.
- night shift placed: 267 loads @ 18cy/load = 4,806cy (18 trucks).

   Phase 1 estimated cummulative waste placed: 249,826cy. Western Ditch, NE Equilization, Eastside beta stockpile, Phase IIIB and PUA-4.PUB-3,HP-3.
- Phase 1 Operations Layer placed. completed. Cumulative total: 21,662
- Phase 2 estimated night shift placed: 0 loads @ 18cy/load = 0 cy.

   Phase 2 Operations Layer placed. daily: 0 cy. Adjusted cy per truckload from 20cy to 18cy based on survey. Cumulative total: 37,188 cy.

2 of 4

Geosynthetics. Estimated cummulative installed quantity by Phase.

- Phase 1 GCL placed:0 sf daily, 307,372 sf cummulative.

## **DAILY PRODUCTION & QUALITY CONTROL REPORT**

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	22-Dec-08	165
		22-000-00	105

- Phase 1 Geomembrane:0 sf daily, 307,372 sf cummulative - Phase 1 Geocomposite: 0 sf daily, 3,372 sf cummulative. - Phase 1 Geotextile: (0) sf daily. 69,340 sf cummulative.

-Phase 2 GCL placed: (0) sf daily, 498,468 sf cummulative.

Phase 2 Geomenbrane: (0) sf daily, 498,468 sf cummulative.
-Phase 2 Geocomposite: (0) sf daily, 520,592 sf cummulative.
-BMI North Landfill GCL placed: (35,200) sf daily, 365,838 sf cummulative.

-BMI North Landfill Geomembrane: (35,200) sf daily, 365,838 sf cummulative.

-BMI North Landfill Geocomposite: (0) sf daily, (305,000) sf cummulative.

Other: None

#### **HEALTH & SAFETY**

Entact H&S Tailgates Safety Topic: Eastside: None

Safety Topic: CAMU, Day: Travel safety during the holidays

Eastside and CAMU, Dressing in layers during cold winter

Safety Incidents: None.

Dust Incidents: None.

#### CONSTRUCTION QUALITY ASSURANCE & QUALITY CONTROL

escription of Quality Control Actions Taken Today / Quality Inspectio

<u>Daily CQA Summary</u>..

Monitored the Installation of geosynthetics on the North BMI Landfill

Monitored installation of waste material in Phase I on the.

Monitored protective cover placement on BMI North Landfill.

Monitored the placement of Phase IIIB maerial in phase 1.

Continued review and updating of project documents and database to facilitate reporting.

## ISSUES AND/OR ITEMS OF DISCUSSION

None

ITE VISITORS				
Name	Organization	Purpose of Visit		
AND A LOCAL LINE TRANSPORTED TO				
AND THE RESIDENCE OF THE PROPERTY OF THE PROPE				

Report Prepared By / Title

Signature

Chris White, Assistant Construction Manager

23-Dec-08

Ver 1.1 11/07

# Basic Remediation Company 875 West Warm Springs Road Henderson, Nevada 89011

## **DAILY PRODUCTION & QUALITY CONTROL REPORT**

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	22-Dec-08	164
0	0	22-Dec-06	

## **DAILY PHOTO LOG**

Photo 1



East Side: Mixing wet material into the dry ponds

Photo 2

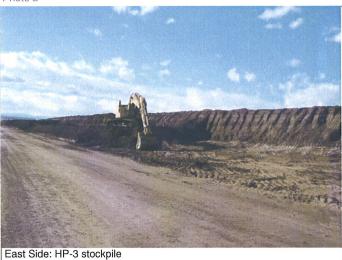


Photo 3



CAMU: 200,000cy stockpile, screening of 1-inch minus.

Photo 4



CAMU: BMI Landfill North, First lift push-out and sub-grade preparation.

Ver 1.1 11/07 4 of 4
