

**Basic Remediation Company**875 West Warm Springs Road  
Henderson, Nevada 89011**DAILY PRODUCTION & QUALITY CONTROL REPORT**

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	30-Dec-08	170

**PROJECT POINTS OF CONTACT**

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranajit Sahu	sahuron@earthlink.net	702-567-0400
CONST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.c	970-260-5886
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolution	720-641-8660

**WEATHER CONDITIONS**

Conditions				Temp (°F)	Wind	Add'l Readings	
AM	Sunny/Clear	PM	Sunny/Clear	Low 38		Precip. (in)	
				High 55	0mph	Humidity (%)	

Additional Weather Comments

Clear Night. Variable wind light 0 - 5 mph.

**ON-SITE WESTON PERSONNEL**

Name	Position	Trade / Work Performed	Y/N	
Dick Laubinger	Construction Manager	Construction Management Services.	Y	
Dan Brennecke	Project Manager. CM	Construction Management Services.	N	
Richard Davis	Project Engineer	Construction Management Services.	Y	
Chris White	Assist. Const. Mgr	Construction Management Services.	Y	
Wayne Hodgson	Assist. Const. Mgr	Construction Management Services.	Y	
Kevin Cooke	Assist. Const. Mgr	Construction Management Services.	Y	
June Laubinger	Admin Assistant	Construction Management Services.	Y	

**ON-SITE GEOSYNTEC PERSONNEL**

Name	Position	Trade / Work Performed	Y/N	
Greg Corcoran	Design Engineer	Oversight	N	
Dan Street	QA Manager	Oversight	Y	
Jim Cox	QA/QC Supervisor	Oversight	N	
Rebecca Flynn	Engineer	Oversight	N	
Wayne Wofford	QA/QC Tech	Oversight	Y	
Roland Derosier	QA/QC Tech	Oversight	N	
Camon Liddell	QA/QC Tech	Oversight	Y	
Jeremy Osborn	QA/QC Tech	Oversight	Y	
Victor Heredia	QA/QC Tech	Oversight	Y	

**ON-SITE SUPPORT PERSONNEL**

Name	Position	Trade / Work Performed	Y/N	
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N	
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring.	N	
Jerry Fauchaux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N	

**OVERSITE PERSONNEL**

Name	Position	Trade / Work Performed	Y/N	
Mark Eizman, ASW	Inspector	Liner Inspector	N	
Devin Gordon, McGinley	Oversight	For NDEP	Y	
Dock Kim, ATC	Field Observation	For AIG	Y	
Joe Ludlow, ASW	Inspector	Liner Inspector	N	
Steve Morrow, ASW	Inspector	Liner Inspector	N	
Brian Rakvica	Inspector	NDEP	N	
PBS&J, Survey	Surveyors	Surveying, QA	N	

**ON-SITE CONTRACTOR PERSONNEL**

Name	Company	Trade / Work Performed	Y/N	
Erik Geringer	Entact	Project Manager	Y	
Josh Carrol	Entact	Asst Project Manager	Y	
Russ Karnes	Entact	Eastside, Superintendent	Y	
Michael Carlson	Entact	Engineer	Y	
Joe Curilla	Entact	Health & Safety Officer	Y	
Timothy Stadt	Entact	Health and Safety Technician	N	
	Entact	26 Equipment Operators & Truck Drivers	Y	
Ed Long	Entact	CAMU, Superintendent	Y	
Lance Bruce	Entact	Health & Safety Officer	Y	
Terry Harper	Entact	CAMU, Superintendent	Y	
Rick McIntire	Entact	CSP, Safety	N	
Dale Walsh	Converse	CSP, Safety	N	

# DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	30-Dec-08	170

Eli Blackburn	Entact	Asst Project Manager	N	
	Environmental Specialties, Inc	1 Liner Superintendent	Y	
	Environmental Specialties, Inc	12 Laborers/ Seamers	Y	
	Kenney Survey	CAMU	N	
	ABC Survey	Eastside/CAMU, Mohawk Drive.	Y	

## ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (10)		CAMU	-	-	-	-
JD D400 Dump Trucks (9)		Eastside	-	-	-	-
CAT 324D long stick excavator		CAMU	-	-	-	-
CAT D8R Dozer with disc		Eastside	-	-	-	-
CAT 345 excavator, (3)		Eastside	-	-	-	-
CAT 330 Excavator		Eastside	-	-	-	-
Case double pan scrapers.		Eastside	-	-	-	-
CAT D6 LGP Dozer (1)		Eastside				-
Water Trucks (2)		Eastside				-
637/631 Cat Scrapers (2)		CAMU				-
CAT 16H Grader		CAMU				-
CAT D-10 Dozer		CAMU				-
CAT Water Trucks (2)		CAMU				-
CAT D-6 Dozer, (2)		CAMU				-
CAT 14H Grader		CAMU				-
Gradall		CAMU				-
JLG		CAMU				-
IR Smooth drum Roller		CAMU, Phase 1				-
Tenent Street Sweeper		Eastside and CAMU				-
Bomag Smooth drum Roller		CAMU, Phase 1				-
Chieftain 1400 Powerscreener		Eastside, screening 1" minus				-
						-

## MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOM	Purpose	Delivery Verification			
					to date	Cty	Spec	Tags
GCL	CETCO	0	rolls	For CAMU, On site		506		
Geocomposite	Agru	0	rolls	For CAMU, On site		599		
Geomembrane	Agru	0	rolls	For CAMU, On site		192		

## WORK COMPLETED

Description of Work Executed Today

### Eastside Mixing and Drying Activity:

- Day Shift:
- Continue excavating and drying material at Parcel 7A ponds.
- Continue running sprinklers on Parcel 7A, PUD ponds.
- Continued Mohawk Drive Parcels, prewatering areas. Began Surficial scrape.
- Night Shift:
- Continue loading/hauling material from the HP-3/HP-2 stockpile and PUB-3, (17 trucks).

### CAMU Activity:

- Day Shift:
- ESI continued placing GCL and Geomembrane on BMI North Landfill.
- Continue subgrade preparation on BMI North Landfill.
- Continue screening cover soil for use at the BMI North Landfill.
- Continue hauling and spreading 1" minus material, first lift on BMI North Landfill.
- Night Shift:
- Place material hauled from eastside in Phase I.

### Embankment

- Phase 1 embankment, complete.
- Phase 1 estimated cumulative embankment placed: 0 cy
- Phase II embankment, complete.

### Waste Placement

- Phase 1 estimated daily waste placed: 0 loads @ 20cy/load = 0cy.
- night shift placed: 246 loads @ 18cy/load = 4,428cy (17 trucks).
- Phase 1 estimated cumulative waste placed: 263,830 cy. Western Ditch, NE Equilization, Eastside beta stockpile, Phase IIIB and PUA-4, PUB-3, HP-3.
- Phase 1 Operations Layer placed, completed. Cumulative total: 21,662
- Phase 2 estimated night shift placed: 0 loads @ 18cy/load = 0 cy.
- Phase 2 Operations Layer placed, daily: 0 cy. Cumulative total: 37,188 cy.

### Geosynthetics. Estimated cumulative installed quantity by Phase.

- Phase 1 GCL placed: 0 sf daily, 307,372 sf cumulative.
- Phase 1 Geomembrane: 0 sf daily, 267,372 sf cumulative.

## DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	30-Dec-08	170

- Phase 1 Geomembrane: 0 sf daily, 307,372 sf cumulative
- Phase 1 Geocomposite: 0 sf daily, 3,372 sf cumulative.
- Phase 1 Geotextile: (0) sf daily, 69,340 sf cumulative.
- Phase 2 GCL placed: (0) sf daily, 498,468 sf cumulative.
- Phase 2 Geomembrane: (0) sf daily, 498,468 sf cumulative.
- Phase 2 Geocomposite: (0) sf daily, 520,592 sf cumulative.
- BMI North Landfill GCL placed: (40,000) sf daily, + 12-29-08 (45,000), 450,838 sf cumulative.
- BMI North Landfill Geomembrane: (40,000) sf daily + 12-29-08 (45,000), 450,838 sf cumulative.
- BMI North Landfill Geocomposite: (0) sf daily, (305,000) sf cumulative.

**Other:** Received additional truckload of 42" RCP storm pipe.

## HEALTH & SAFETY

Description of Health &amp; Safety Actions Taken Today / Safety Inspections Conducted

**Entact H&S Tallgates**

**Safety Topic:** Eastside: Discussed working around heavy equipment and knowing where the blind spots area.

**Safety Topic:** CAMU, **Day:** Discussed working around heavy equipment and knowing where the blind spots are.

Eastside and CAMU, Night: Discussed the hazards of working on decon pad the hazards of working when ice exists on the ground and other surfaces.

**Safety Incidents:** None. Unrelated to Entact a two car accident occurred during the night shift in the middle of Boulder Hwy. Entact called a stop work while authorities took care of the accident.

Dust Incidents: None.

## CONSTRUCTION QUALITY ASSURANCE & QUALITY CONTROL

Description of Quality Control Actions Taken Today / Quality Inspections Conducted

### Daily CQA Summary..

Monitored waste placement and observed proofrolling in phase I. Night Shift.

Monitored the installation of geosynthetics at BMI North Landfill. Day shift.

Monitored the placement of 1" minus material, first lift on geosynthetics.

Continue review of and updating of project documents and database to facilitate reporting.

## ISSUES AND/OR ITEMS OF DISCUSSION

Discussion of Issues / Concerns / Conversations / Topics

None

## SITE VISITORS

[illegible]

Report Prepared By / Title

**Richard Laubinger, Construction Manager**

Date Prepared

30-Dec-08

Signature \_\_\_\_\_



## Basic Remediation Company


875 West Warm Springs Road  
Henderson, Nevada 89011

### DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
<b>6389</b> 0	<b>BRC Eastside Common Areas Soils Remediation</b> 0	30-Dec-08	<b>170</b>

### DAILY PHOTO LOG

Photo 1

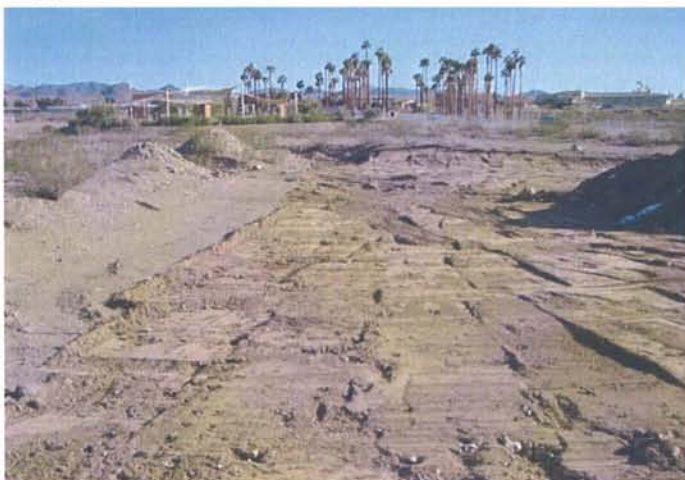

Mohawk, surficial scrape.

Photo 2



Mohawk, surficial scrape.

Photo 3



CAMU: BMI North Landfill geocomposite and first cover layer of 1" minus soils.

Photo 4



CAMU: BMI North Landfill geocomposite layer.
