



DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation	03-Mar-09	233

PROJECT POINTS OF CONTACT

Position	Name	E-Mail Address	Phone No.
BRC PROJECT MANAGER	Lee Farris	lfarris@landwellco.com	702-567-0400
BRC PROJECT MANAGER	Ranjit Sahu	rsahur@earthlink.net	702-567-0400
COIST. PROJECT MANAGER	Dan Brennecke	Dan.Brennecke@westonsolutions.com	970-260-5888
Construction Manager	Richard Laubinger	Richard.Laubinger@westonsolutions.com	720-641-8660

WEATHER CONDITIONS

Conditions	Temp	Wind	Add'l Readings
Atm Cloudy	Low 50 High 74	SW 10mph	Precip 0.00 Humidity 90

National Weather Service

Winds in PM 10 - 15 mph.

ON-SITE WESTON PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Dick Laubinger	Construction Manager	Construction Management Services.	Y
Dan Brennecke	Project Manager, CM	Construction Management Services.	N
Richard Davis	Project Engineer	Construction Management Services.	Y
Chris White	Assist. Const. Mgr	Construction Management Services.	Y
Wayne Hodgson	Assist. Const. Mgr	Construction Management Services.	Y
Kevin Cooke	Assist. Const. Mgr	Construction Management Services.	Y
June Laubinger	Admin Assistant	Construction Management Services.	Y

ON-SITE GEOSYNTEC PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Greg Corcoran	Design Engineer	Oversight	N
Dan Street	QA Manager	Oversight	Y
Jim Cox	QA/QC Supervisor	Oversight	N
Roberta Flynn	Engineer	Oversight	N
Sam Campbell-Nelson	QA/QC Tech	Oversight	Y
Roland Desrosier	QA/QC Tech	Oversight	Y
Cameron Liddell	QA/QC Tech	Oversight	Y
Jeremy Osborn	QA/QC Tech	Oversight	Y
Victor Heredia	QA/QC Tech	Oversight	Y

ON-SITE SUPPORT PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Doug Herlocker, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N
Becky Dano, Tetra Tech	Air Monitoring Specialist	Air Monitoring	Y
Jerry Fauchoux, Tetra Tech	Air Monitoring Specialist	Air Monitoring	N

OVERSITE PERSONNEL

Name	Position	Trade / Work Performed	Y/N
Mark Elzman, ASW	Inspector	Linear Inspector	Y
Devon Gordon, McKinley	Oversight	For NDEP	Y
Dock Kim, ATC	Field Observation	For AIG	N
Joe Ludlow, ASW	Inspector	Linear Inspector	N
Steve Morrow, ASW	Inspector	Linear Inspector	N
Brian Rakvica	Inspector	NDEP	N
PBS&J, Survey	Surveyors	Survey	N

ON-SITE CONTRACTOR PERSONNEL

Name	Company	Trade / Work Performed	Y/N
Erik Geringer	Entact	Project Manager	N
Jeremy Schissler	Entact	Acting Project Manager	Y
Josh Carroll	Entact	Asst Project Manager	Y
Michael Carlson	Entact	Engineer	Y
Joe Outila	Entact	Health & Safety Officer	Y
Timothy Stadl	Entact	Health and Safety Technician	Y
Ed Long	Entact	48 Equipment Operators & Truck Drivers	Y
Lance Bruce	Entact	CAMU, Superintendent	Y
Terry Harper	Entact	Health & Safety Officer	Y
Rick McInire	Entact	CAMU, Superintendent	Y
Dale Walsh	Converse	CSP, Safety	N
El Blackburn	Entact	Asst Project Manager	Y
	Environmental Specialties, Inc.	1 Linear Superintendent	N
	Environmental Specialties, Inc.	12 Laborers/ Steamers	N
Carol McInire	Entact	Health & Safety Officer	Y
Roger Wagner	Entact	Eastside, Superintendent, Night Shift.	Y
	ABC Survey	Eastside/CAMU, Mohawk Drive.	N
	Foundation Pile, Inc.	Demobilized.	N

ON-SITE EQUIPMENT

Equipment	Vendor / Tag No.	Work Performed				
CAT D400E Dump Truck (10)		CAMU	-	-	-	-
JD D400 Dump Trucks (8)		Eastside	-	-	-	-
CAT 324D long stick excavator		Eastside	-	-	-	-
CAT D8R Dozer with disc		Eastside	-	-	-	-
CAT 345 excavators, (5)		Eastside and CAMU	-	-	-	-
CAT 330 Excavator		CAMU	-	-	-	-
Case double pan scrapers.		Eastside, demobilized.	-	-	-	-
CAT D6 LGP Dozer (1)		Eastside	-	-	-	-
Water Trucks (2)		Eastside	-	-	-	-
JD450 Dozer		CAMU	-	-	-	-
CAT 16H Grader		CAMU	-	-	-	-
CAT D-10 Dozer		CAMU	-	-	-	-
Water Trucks (2)		CAMU	-	-	-	-
CAT D-8 Dozer, (2)		CAMU	-	-	-	-
CAT 14H Grader		CAMU	-	-	-	-
Grasshopper		CAMU	-	-	-	-
JLG		CAMU	-	-	-	-
IR Smooth drum Roller		CAMU, Phase 1	-	-	-	-
Tenent Street Sweeper		Eastside and CAMU	-	-	-	-
Bomag Smooth drum Roller		CAMU, Phase 1	-	-	-	-
Chieftain 1400 Powerscreener		Eastside, screening 1" & 6" minus	-	-	-	-
(1) Crane		Sheet pile driving. Installed, (1) Crane remains.	-	-	-	-

MATERIAL HANDLING (ON-SITE DELIVERY / REMOVAL)

Material	Vendor	Today	UOM	Purpose	Delivery Vehicle
GCL	CETCO	60	rolls	For CAMU, On site	1202

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No. Contract No.	Project Title - Location		Day of Report	Report No.
6389	BRC Eastside Common Areas Soils Remediation		03-Mar-09	233
Geocomposite	Agro	0 rolls	For CAMU, On site	2292
Geomembrane	Agro	0 rolls	For CAMU, On site	448

WORK COMPLETED

Number of Work & Volume Today:

Eastside Mixing and Drying Activity:

Day Shift:

- Powerscreener moved to beta ditch screening 1" & 6" minus material.
- SW-7, excavator loading out wet material (2) haul trucks hauled to PUE-5 pond for drying.
- PUC-5, remedial waste from north berm, top and south slope.
- Continued haul truck modifications.

Night Shift:

- Continued hauling material from the Beta ditch.
- Continued hauling material from Parcel 7A ponds.

CAMU Activity:

Day Shift:

- Continued excavating slit trenches NW-2 & NW-3, trash and debris, gravel and paper products watered down and hauled.
- Slit trench SW-2, continued excavating and encountered additional pyrophoric material.
- Continued 42" RCP storm drain pipe system installation.
- Phase IIIA, placed operations layer first lift of 1" minus material on south slope and the second lift, 6" minus on west side of floor.

Night Shift:

- Continued placing material in Phase II.
- Continued hauling 6" minus operations layer material to Phase IIIA.

Embankment

- Phase I embankment, complete.
- Phase I estimated cumulative embankment placed: 0 cy
- Phase II embankment, complete.

Other: CAMU: Fence contractor on site installing temporary fence tie-in on Findley property
Liner deliveries.

Inspections: Slit trenches NW-2, trash, paper and gravel material
NW-3 trash, gravel, small amount of paper. Green/yellow material remaining is to hard to remove. A concrete breaker will be needed to breakup and size for removal.

Estimated Waste Placement (Estimated volumes do not account for shrinkage due to loss of moisture on wet ponds)

Phase I

Previous Daily Cumulative =	291,200	cy
Operations layer placed (completed) for liner certification. = 21,662	0	cy
Daily Day shift waste placed today: Phase IV,V scape & Phase IIIB trench excavation. 0 loads @ 20 cy/load (0 trucks) =	0	cy
Daily Night shift placed today: 0 loads @ 18cy/load (0 trucks) =	0	cy
To Date Phase I estimated cumulative waste placed =	291,200	cy

Phase II

Previous Daily Cumulative =	340,106	cy
Operations layer placed (completed) for liner certification. = 37,188	0	cy
Daily Day shift waste placed today: Phase IIIB (0) loads @ 18 cy/load (0) trucks =	0	cy
Daily Day shift waste placed today: Slit Trenches, (116) loads @ 18cy/load (4) trucks =	2,088	cy
Daily Night shift placed today: (77) loads @ 18cy/load (8) trucks =	1,386	cy
To Date Phase II estimated cumulative waste placed =	343,580	cy

Phase IIIA

Previous Daily Cumulative =	17,514	cy
Operations layer placed directly in Phase IIIA today: (0) loads @ 18 cy/load (0) trucks =	0	cy
Operations layer staged in Phase IIIA for day placement (ongoing) for liner certification: (201) loads @ 18 cy/load (19) trucks =	3,618	cy
Daily Day shift waste placed today: (0) loads @ 18 cy/load (0) trucks =	0	cy
Daily Night shift waste placed today: (0) loads @ 18cy/load (0) trucks =	0	cy
To Date Phase IIIA estimated cumulative waste placed =	21,132	cy

Cumulative Total To Date All Phases =	655,912	cy	Estimated Waste at Completion (cy)	2,050,000	% Complete	32.0%
--	----------------	-----------	---	------------------	-------------------	--------------

Geosynthetics Placed

Phase I (complete)	Previous	Placed	Cumulative
GCL	307,372	0	307,372
Geomembrane	307,372	0	307,372
Geocomposite	307,372	0	307,372
Geotextile	69,340	0	69,340
Phase II (complete)	Previous	Placed	Cumulative
GCL	498,468	0	498,468
Geomembrane	498,468	0	498,468
Geocomposite	520,592	0	520,592
Geotextile	0	0	0
Phase IIIA	Previous	Placed	Cumulative
GCL	221,000	0	221,000
Geomembrane	221,000	0	221,000
Geocomposite	221,000	0	221,000
Geotextile	20,000	0	20,000
Phase IIIB	Previous	Placed	Cumulative
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase IV	Previous	Placed	Cumulative
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0
Phase V	Previous	Placed	Cumulative
GCL	0	0	0
Geomembrane	0	0	0
Geocomposite	0	0	0
Geotextile	0	0	0

Basic Remediation Company


875 West Warm Springs Road
Henderson, Nevada 89011

DAILY PRODUCTION & QUALITY CONTROL REPORT

Project No./Contract No.	Project Title / Location	Day of Report	Report No.
6389 0	BRC Eastside Common Areas Soils Remediation 0	03-Mar-09	233

DAILY PHOTO LOG

Photo 1

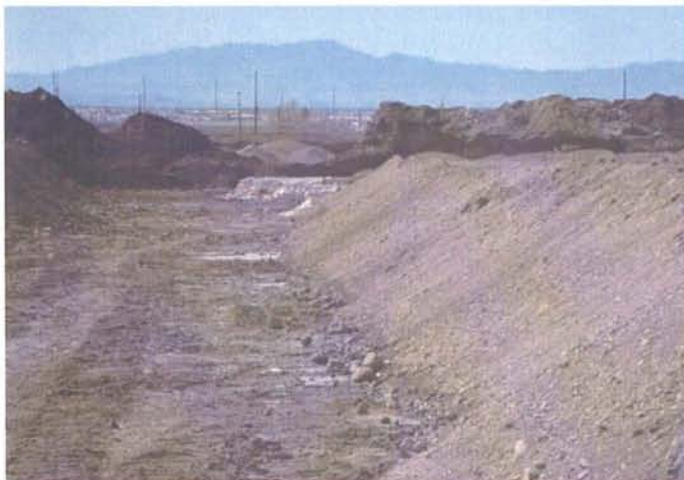

Eastside: SW-2, wet pond.

Photo 2




Eastside: PUE-5 dry pond.

Photo 3



Eastside: PUE-5.

Photo 4

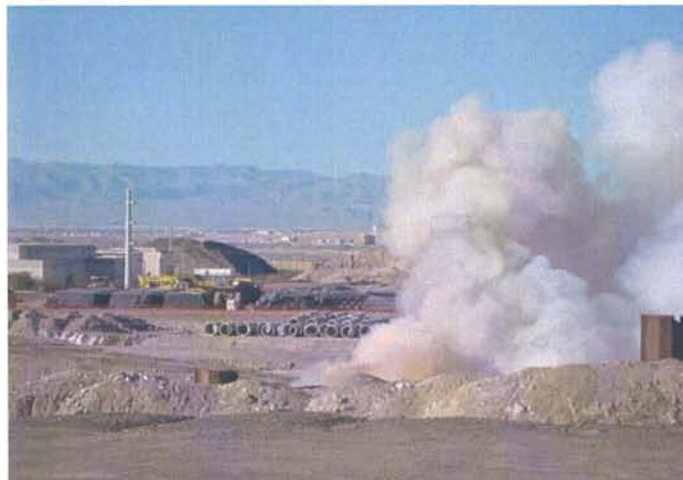

CAMU: Slit trench, SW-2.
